

CERTIFICATE AGAINST USE OF  
ASBESTOS-CONTAINING MATERIAL

The undersigned Contractor under Contract No. \_\_\_\_\_  
dated \_\_\_\_\_ between the United States of America and  
\_\_\_\_\_ for \_\_\_\_\_  
\_\_\_\_\_ ,

in accordance with specification Section 01 50 00: TEMPORARY  
CONSTRUCTION FACILITIES AND CONTROLS, AND MISCELLANEOUS PROVISIONS,  
paragraph "ASBESTOS-CONTAINING MATERIALS (ACM)", hereby certifies  
neither it nor any of its subcontractors at any tier has used  
asbestos-containing materials in the construction of the herein  
described project. I am the \_\_\_\_\_  
\_\_\_\_\_

for the Contractor, and know by first-hand knowledge, and/or by  
information and belief that the foregoing is true and correct.

Date: \_\_\_\_\_

Name: \_\_\_\_\_

Position \_\_\_\_\_


Company Name: \_\_\_\_\_

Address: \_\_\_\_\_

\_\_\_\_\_  
\_\_\_\_\_

Notes:

1. Window sill height shall be 3'-0" from floor line.
2. Lintel shall be 8" high U-block w/2-#4 bars.
3. Steel door frame shall be 3'-9" in height, filled with grout. The frame shall include reinforcement of hinges with plaster guard.
4. Concrete footing shall be of same depth as required by structure and sufficient to support masonry.
5. Interior insulation shall be installed up to 3'-0" from floor line.
6. Gypsum wall board must include at least one joint with finishing.
7. Pipe sleeve with pipe and insulation required for sample panel is in addition to pipe insulation sample board required in technical provisions.

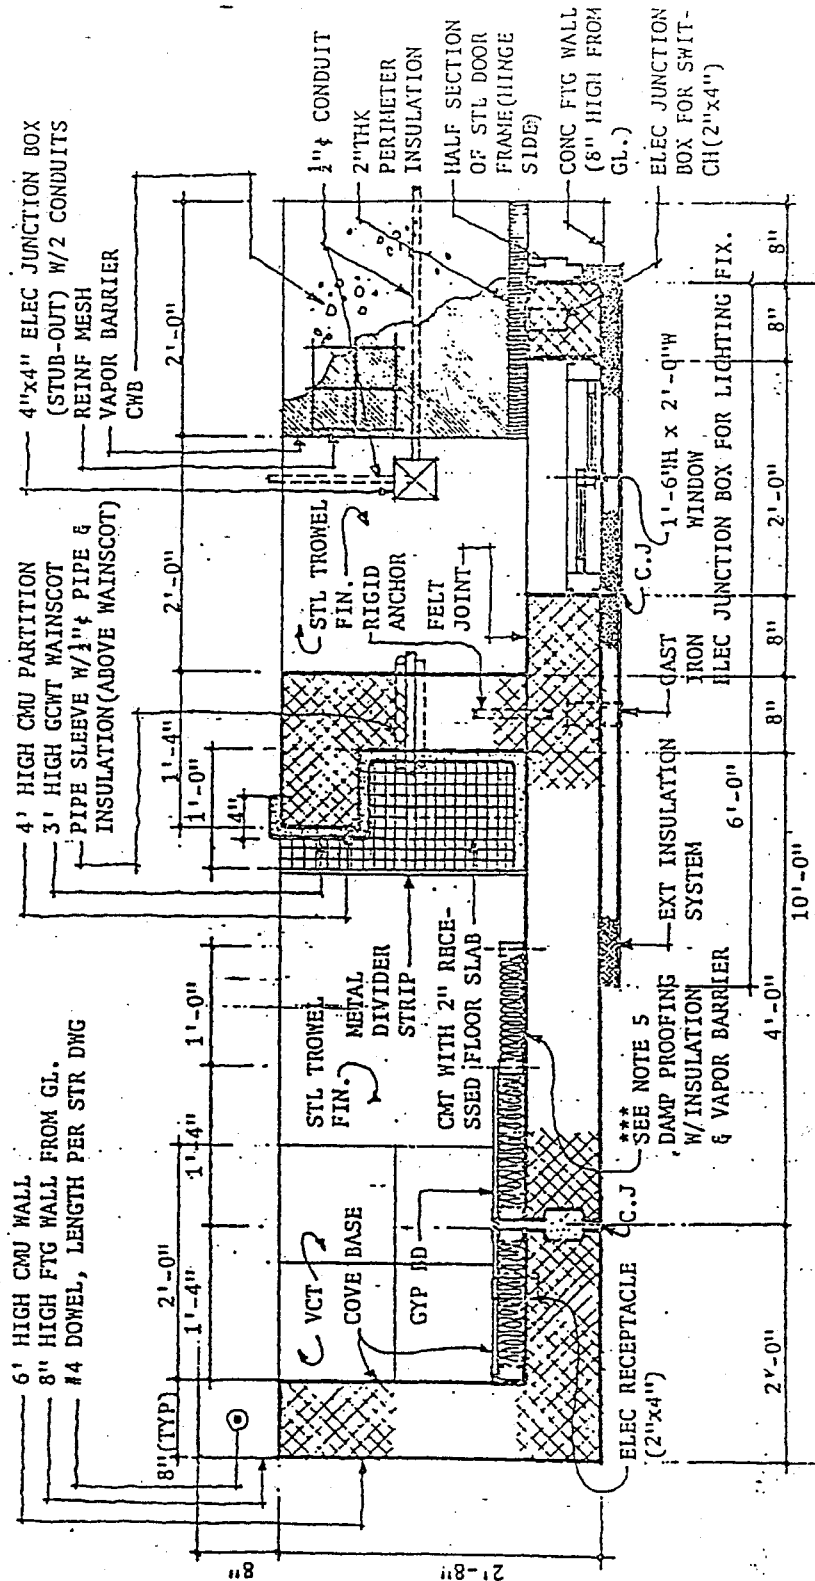

SAMPLE PANEL PLAN

PLATE #1  
no. scale

The use of signs to identify Corps managed or supervised design, construction, and rehabilitation projects - both for military and civil works - is an important part of efforts to keep the public informed of Corps work. For this purpose, a construction project sign package has been adopted. This package consists of two signs: one for project identification and the other to show on-the-job safety performance of the contractor.

These two signs are to be displayed side by side and mounted for reading by passing viewers. Exact placement location will be designated by the contracting officer's representative.

The panel sizes and graphic formats have been standardized for visual consistency throughout all Corps operations.

Panels are fabricated using HDO plywood or aluminum with dimensional lumber uprights and bracing. The sign faces are nonreflective vinyl.

All legends are to be die-cut or computer-cut in the sizes and typefaces specified and applied to the white panel background following the graphic formats shown on pages 16-2 and 16-3. The Communication Red panel on the left side of the construction project sign with Corps Signature (reverse version) is screen-printed onto the white background.

A display of these two signs is shown on the following two pages. Mounting and fabrication details are provided on page 16-4.

Special applications or situations not covered in these guidelines should be referred to the district Sign Program Manager.

**By ECB No. 2020-1, all USACE projects will display signage that features the Army Star logo as part of the overall USACE construction project signage, example shown on page 16-2a.**

Below are two samples of the Construction Project Identification sign showing how this panel is adaptable for use to identify either military (top) or civil works projects (bottom). The graphic format for this 4'x 6' sign panel follows the legend guidelines and layout as specified below. The large 4'x 4' section of the panel on the right is to be white with black legend. The 2'x 4' section of the sign on the left

with the full Corps Signature (reverse version) is to be screen-printed Communication Red on the white background. The designation of a sponsor in the area indicated is optional with Military or Civil Works construction signs. Signs may list one sponsoring entity. If agreement on a sponsor designation cannot be achieved, the area should be left blank.

This sign is to be placed with the Safety Performance sign shown on the following page. Mounting and fabrication details are provided on page 16-4.

Special applications or situations not covered in these guidelines should be referred to the district Sign Program Manager.

Legend Group 1: One- to two-line description of Corps relationship to project.  
Color: White  
Typeface: 1.25" Helvetica Regular  
Maximum line length: 19"

Legend Group 2: Division or District Name (optional). Placed below 10.5" reverse Signature (6" Castle).  
Color: White  
Typeface: 1.25" Helvetica Regular

Legend Group 2a: One- to three-line identification of Military or Civil Works sponsor (optional). Place below Corps Signature to cross-align with Group 5a-b.  
Color: White  
Typeface: 1.25" Helvetica Regular  
Maximum line length: 19"



Legend Group 3: One- to three-line project title legend describes the work being done under this contract.  
Color: Black  
Typeface: 3" Helvetica Bold  
Maximum line length: 42"

Legend Group 4: One- to two-line identification of project or facility (civil works) or name of sponsoring department (military).  
Color: Black  
Typeface: 1.5" Helvetica Regular  
Maximum line length: 42"

Cross-align the first line of Legend Group 4 with the first line of the Corps Signature (US Army Corps) as shown.

Legend Groups 5a-b: One- to five-line identification of prime contractors including: type (architect, general contractor, etc.), corporate or firm name, city, state. Use of Legend Group 5 is optional.  
Color: Black  
Typeface: 1.25" Helvetica Regular  
Maximum line length: 21"

All typography is flush left and rag right, upper and lower case with initial capitals only as shown. Letter- and word-spacing to follow Corps standards as specified in Appendix D.

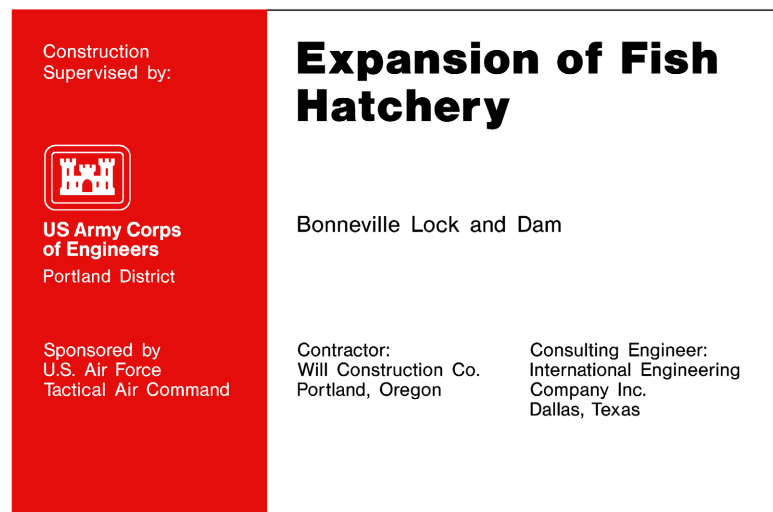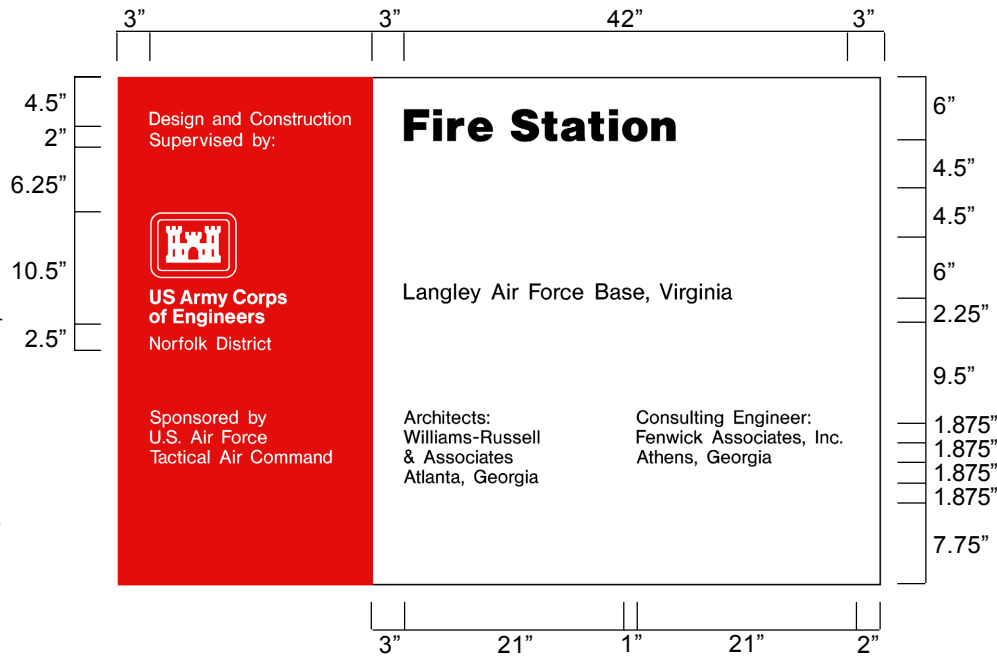

Sign Type	Legend Size (A)	Panel Size	Post Size	Specification Code	Mounting Height	Color Bkg/Lgd
CID-01	various	4'x6'	4"x4"	HDO-3	48"	WH-RD/BK

Design and Construction Supervised by:

US Army Corps of Engineers  
Los Angeles District

Sponsored by:

Contractor:

Consulting Engineer:

Each contractor's safety record is to be posted on Corps managed or supervised construction projects and mounted with the Construction Project Identification sign specified on page 16-2.

The graphic format, color, size and typefaces used on the sign are to be reproduced exactly as specified below. The

title with First Aid logo in the top section of the sign, and the performance record captions are standard for all signs of this type. Legend groups 2 and 3 below identify the project and the contractor and are to be placed on the sign as shown.

Safety record numbers are mounted on individual metal plates and are screw-

mounted to the background to allow for daily revisions to posted safety performance record.

Special applications or situations not covered in these guidelines should be referred to the district Sign Program Manager.

Legend Group 1: Standard two-line title "Safety is a Job Requirement" with 8" (outside diameter) Safety Green first aid logo.  
Color: To match Pantone system 347  
Typeface: 3" Helvetica Bold  
Color: Black


Legend Group 2: One- to two-line project title legend describes the work being done under this contract and name of host project.  
Color: Black  
Typeface: 1.5" Helvetica Regular  
Maximum line length: 42"

Legend Group 3: One- to two-line identification: name of prime contractor and city, state address. Color: Black  
Typeface: 1.5" Helvetica Regular  
Maximum line length: 42"


Legend Group 4: Standard safety record captions as shown.  
Color: Black  
Typeface: 1.25" Helvetica Regular

Replaceable numbers are to be mounted on white .060 aluminum plates and screw-mounted to background.  
Color: Black  
Typeface: 3" Helvetica Regular  
Plate size: 2.5" x 4.5"

All typography is flush left and rag right, upper and lower case with initial capitals only as shown. Letter- and word-spacing to follow Corps standards as specified in Appendix D.

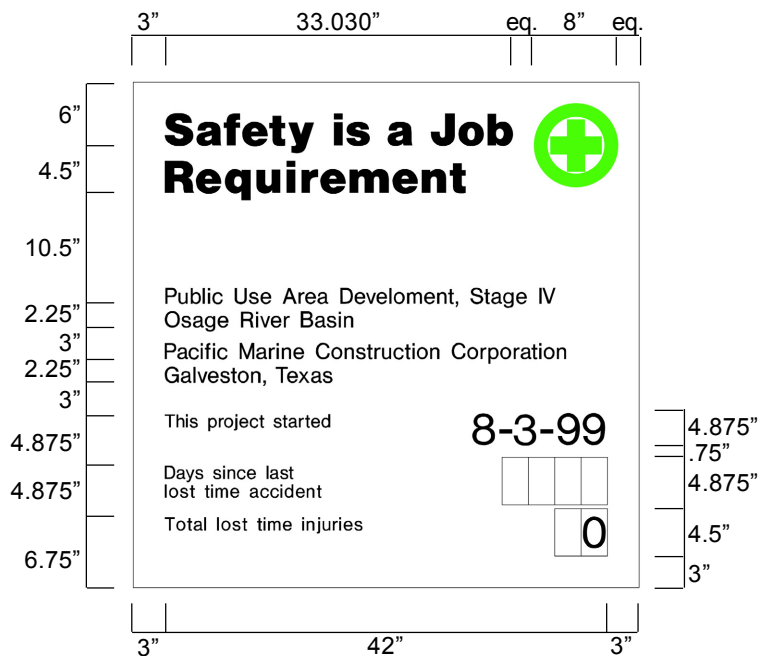

Sign Type	Legend Size (A)	Panel Size	Post Size	Specification Code	Mounting Height	Color Bkg/Lgd
CID-02	various	4'x4'	4"x4"	HDO-3	48"	WH/BK-SG

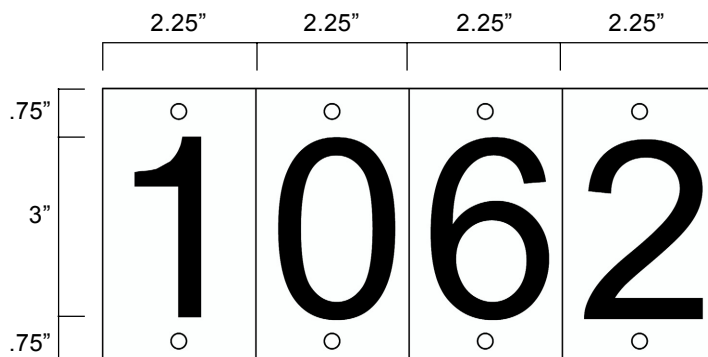

All Construction Project Identification signs and Safety Performance signs are to be fabricated and installed as described below. The signs are to be erected at a location designated by the contracting officer representative and shall conform to the size, format, and typographic standards shown on pages 16-2 and 16-3. Detailed specifications

for HDO plywood panel preparation are provided in Appendix B.

Shown below the mounting diagram is a panel layout grid with spaces provided for project information. Photocopy this page and use as a worksheet when preparing sign legend orders.

For additional information on the proper method to prepare sign panel graphics, contact the district Sign Program Manager.

The sign panels are to be fabricated from .75" High Density Overlay Plywood. Panel preparation to follow HDO specifications provided in Appendix B.

Sign graphics to be prepared on a white nonreflective vinyl film with positionable adhesive backing.

All graphics except for the Communication Red background with Corps Signature on the project sign are to be die-cut or computer-cut nonreflective vinyl, prespaced legends prepared in the sizes and typefaces specified and applied to the background panel following the graphic formats shown on pages 16-2 and 16-3.


The 2'x 4' Communication Red panel (to match Pantone system 032) with full Corps Signature (reverse version) is to be screen-printed on the white background. Identification of the district or division may be applied under the signature with white cut vinyl letters prepared to Corps standards.

Drill and insert six (6) .375" T-nuts from the front face of the HDO sign panel. Position holes as shown. Flange of T-nut to be flush with sign face.

Apply graphic panel to prepared HDO plywood panel following manufacturers' instructions.

Sign uprights to be structural grade 4" x 4" treated Douglas Fir or Southern Yellow Pine, No.1 or better. Post to be 12' long. Drill six (6) .375" mounting holes in uprights to align with T-nuts in sign panel. Countersink (.5") back of hole to accept socket head cap screw (4" x .375").

Assemble sign panel and uprights. Imbed assembled sign panel and uprights in 4' hole. Local soil conditions and/or wind loading may require bolting additional 2" x 4" struts on inside face of uprights to reinforce installation as shown.

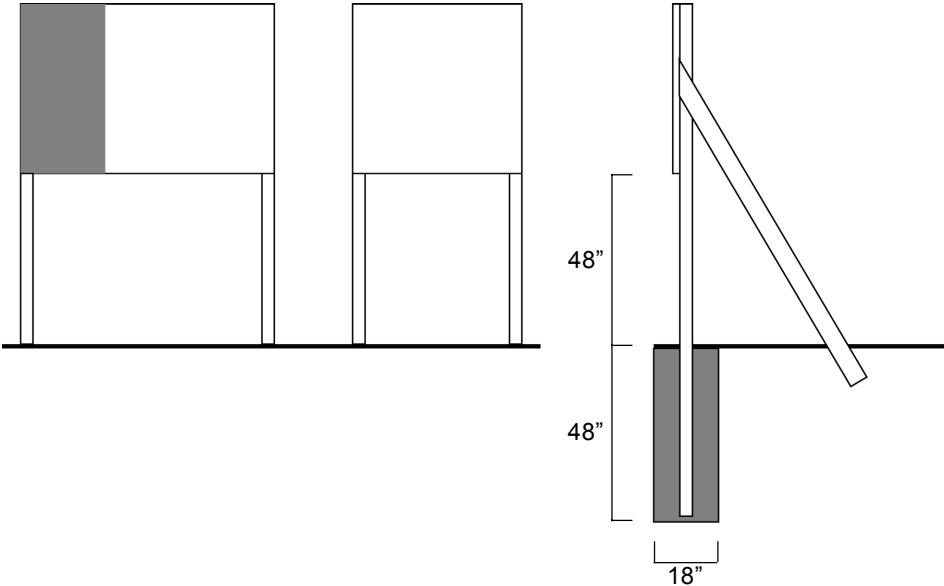

Construction Project Identification Sign  
Legend Group 1: Corps Relationship

1. \_\_\_\_\_
2. \_\_\_\_\_

Legend Group 2: Division/District Name

1. \_\_\_\_\_
2. \_\_\_\_\_

Legend Group 2a: Military/Civil Works Sponsor

1. \_\_\_\_\_
2. \_\_\_\_\_

Legend Group 3: Project Title

1. \_\_\_\_\_
2. \_\_\_\_\_
3. \_\_\_\_\_

Legend Group 4: Facility Name

1. \_\_\_\_\_
2. \_\_\_\_\_

Legend Group 5: Contractor/A&E

1. \_\_\_\_\_
2. \_\_\_\_\_
3. \_\_\_\_\_
4. \_\_\_\_\_
5. \_\_\_\_\_

Legend Group 5b: Contractor/A&E

1. \_\_\_\_\_
2. \_\_\_\_\_
3. \_\_\_\_\_
4. \_\_\_\_\_
5. \_\_\_\_\_

Safety Performance Sign

Legend Group 2: Project Title

1. \_\_\_\_\_
2. \_\_\_\_\_

Legend Group 3: Contractor/A&E

1. \_\_\_\_\_
2. \_\_\_\_\_
